



AUGUST 2007

MONTHLY PROGRESS REPORT

project partners

PROGRAM DESCRIPTION

The Groundwater Replenishment (GWR) System is a jointly funded project of the Orange County Water District (OCWD) and Orange County Sanitation District (OCSD) with OCWD as the lead or constructing agency. The GWR System is a water supply project designed to ultimately reuse approximately 140,000 acre-feet per year (afy) of advanced treated wastewater (recycled water). The phase currently being constructed will supply approximately 72,000 afy and provide the backbone facilities for future expansion. The GWR System will supplement existing water supplies by providing a new, reliable, high-quality source of water to recharge the Orange County Groundwater Basin (the Basin) and protect the Basin from further degradation due to seawater intrusion. It will also postpone the need for OCSD to construct a new ocean outfall by treating excess storm flows.



The GWR System will be comprised of three major components: (1) Advanced Water Purification Facility (AWPF) and pumping stations; (2) a major pipeline connecting the purification facility to existing recharge basins; and (3) expansion of an existing seawater intrusion barrier. Phase 1 of the GWR System will have a nominal rated product water capacity of 70 million gallons per day (mgd). Timing of future phases will be determined by projected flow requirements for anticipated water demands.

The construction of the GWR System will consist of seven major construction contracts totaling \$410.3 million and a total program budget of \$480.9 million.

For more information regarding the Groundwater Replenishment System, contact our Website at www.gwrssystem.com.

purpose:

The GWR System will be comprised of three major components:

PROJECT HIGHLIGHTS

There are three major components to the GWR System Project:

1. Advanced Water Purification Facility in Fountain Valley - 95% complete.
2. A 13-mile pipeline from Fountain Valley to Anaheim (along the Santa Ana River) - 100% complete.
3. Expansion of the Seawater Intrusion Barrier facilities - 100% complete.

- 1 Advanced Water Purification Facility (AWPF) and pumping stations
- 2 A major pipeline connecting the treatment facilities to existing recharge basins
- 3 Expansion of an existing seawater intrusion barrier.

PROJECTS UNDER CONSTRUCTION



AWPF Microfiltration Cell Backwashing



AWPF Cartridge Filters and
Chemical Storage Area



AWPF Reverse Osmosis Train



AWPF Hydrogen Peroxide
Metering Pumps



AWPF Control Room

Advanced Water Purification Facility (Budget \$305,300,000)

The AWPf contract includes all structures, piping and facilities that are within the boundaries of the OCWD and OCSD treatment site located at Ellis Avenue and Ward Street in Fountain Valley. Facilities include the Screening Facility at OCSD's Plant No. 1, the 96-inch diameter influent pipeline from the Screening Facility to Microfiltration Facility, Microfiltration Facility (86 mgd filtrate), Microfiltration Break Tank, Reverse Osmosis Facility (70 mgd permeate), UV System (70 mgd product), Chemical Feed/Lime Stabilization System, Product Water/Barrier Pump Station, and all yard piping. Included in the AWPf contract will be all electrical, instrumentation, and process control systems (PCS) associated with each facility. The MF and UV equipment was pre-selected by the District and their contracts were assigned to the Contractor.

The AWPf contractor continues finish work on the east and west side microfiltration buildings. Microfiltration membranes have been installed in 24 of the 26 cells and have been processing secondary effluent this past week. The 48 hour testing on the completed microfiltration system will begin within the next two weeks. Microfiltration effluent is being run through the reverse osmosis units (without membranes) so that sequencing can be validated and control loops tuned. Reverse osmosis membranes will be installed later next month. Functional acceptance testing continues in the sulfuric acid threshold inhibitor, citric acid, reverse osmosis clean-in-place, decarbonation and barrier well facilities. The process control system has also been recently fully integrated so that the entire plant is now operated from a single point. Plant start-up and overall project completion is scheduled for November 2007.


GWR System Active Projects Construction Schedule

ID	Project Name	2007					2008							
		Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	
1	Advanced Water Purification Facility	█												

GWR System Construction Schedule

ID	Project Name	2002	2003	2004	2005	2006	2007
1	Southeast Barrier	█	█				
2	Interim Water Purification Facility		█	█			
3	GWR System Unit III Pipeline		█	█	█		
4	GWR System Unit II Pipeline			█	█	█	
5	GWR System Unit I Pipeline			█	█	█	█
6	Barrier Facilities			█	█	█	
7	Advanced Water Purification Facility			█	█	█	█

Project Funding

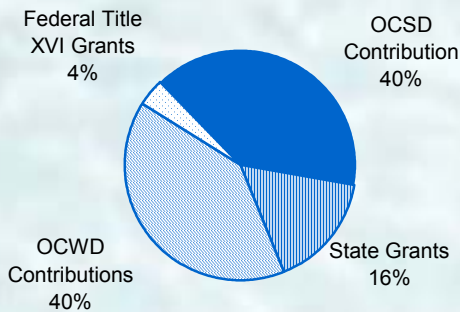

EPA Grant	\$500,000
State Water Resources Control Board Grant	\$5,000,000
US Bureau of Reclamation Grant	\$20,000,000
Department of Water Resources Grant (Prop. 13)	\$30,000,000
Santa Ana Watershed Project Authority Grant (Prop. 13)	\$37,000,000
OCWD Contribution	\$198,560,000
OCSD Contribution	\$198,560,000

Projected vs. Actual Costs

